

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

OX CART/IDEALIST

8899-69
Copy 13 of 13

25X1A

NRO REVIEW COMPLETED

15 APR 1969

MEMORANDUM FOR: Director, CIA Reconnaissance Programs

SUBJECT: Program Progress Report

Forwarded herewith are Program Progress Reports

(5 copies each) for OXCART and IDEALIST for the period

25X1A

1 January 1969 - 31 March 1969.



DONALD H. ROSS
Brigadier General, USAF
Director of Special Activities

Attachments -

As stated 6409-69)

25X1A

25X1A

OX CART/IDEALIST

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION



TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5



8899-69

Page 2

25X1A

25X1A

SAS/O/OSA




(15 April 1969)

Distribution:

- #1 - D/CRP
- #2 - D/CRP
- #3 - D/CRP
- #4 - D/CRP
- #5 - D/CRP
- #6 - DD/S&T Reg (w/o att.)
- #7 - D/SA
- #8 - SAS/O/OSA
- #9 - D/O/OSA
- #10 - IDEA/O/OSA
- #11 - D/M/OSA
- #12 - R&D/OSA
- #13 - RB/OSA

25X1A



OX CART/IDEALIST

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

TOP SECRET

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

6409-69

TAB A, Section 1

25X1A

OX CART

SUMMARY AND PROGRESS

(1 January 1969 - 31 March 1969)

I. GENERAL

A. OX CART

1. AFIGOS (Pentagon) has requested A-12 cost data from Lockheed Aircraft Corporation (LAC) for inclusion in FY-70/ FY-71 NRO budget considerations.

2. The cost data is to reflect three options of costing, as follows:

a. The basic costs for continuing inspection and maintenance of the stored OXCART fleet.

b. The additional costs and timing for bringing one A-12 aircraft to a "ready-fly" condition.

c. The total costs and timing for processing five A-12 aircraft to a "ready-fly" condition.

3. The OXCART sensors and systems will not be exercised. The connotation of "ready-fly" condition being to demonstrate a high-flight, supersonic capability.

25X1D

25X1A

OX CART/IDEALIST

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

6409-69

TAB B, Section 1

Page 2

25X1A

IDEALIST

DEVELOPMENT SUMMARY AND PROGRESS

(1 January 1969 - 31 March 1969)

I. AIRFRAME



25X1D

B. U-2R FLIGHT TEST AND OPERATIONAL TRAINING
SUMMARY (THRU 31 MARCH 1969)

	<u>J.F.M. FLTS</u>	<u>J.F.M. TIME</u>	<u>TOTAL FLTS</u>	<u>TOTAL TIME</u>
1 - 051	13	29.4	108	337.6
2 - 052	3	12.5	58	215.0
3 - 053	16	64.7	84	260.3
4 - 054	23	95.5	84	285.1
5 - 055	34	153.8	90	310.4
6 - 056	--	----	21	47.1
7 - 057	36	126.6	71	285.7
8 - 058	27	126.9	65	247.7
9 - 059	--	----	6	11.0
10 - 060	5	16.6	19	33.5
11 - 061	4	8.4	13	25.0
12 - 062	<u>4</u>	<u>13.5</u>	<u>11</u>	<u>25.7</u>
TOTAL	165	647.9	630	2084.1

25X1A

OXCART/IDEALIST

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

OXCART/IDEALIST

6409-69

25X1A

TAB B, Section 1

Page 3


II. PROPULSION

A. Engine Thrust Management - The effort to develop a satisfactory engine pressure ratio (EPR) curve for determining maximum safe power settings for the J75-P-13B engine at altitude has been completed. As a result of an extensive accumulation of flight test and flight experience data at both Detachments G and H, a final EPR curve was released by Pratt & Whitney engineering on 28 March 1969. No compressor instabilities were incurred throughout the extensive flight experience accumulated to date.

B. Engine Performance Improvement - Unfunded studies by Pratt & Whitney during the third quarter FY-69 have analysed several alternate means of providing varying degrees of improved performance of the J75-P-13B engine. Lockheed will now determine the effect these engine modifications will have on the U-2R aircraft. The studies by Lockheed will be conducted under the DNRO approved FY-69 funding for U-2R engine performance improvement.

III. PAYLOAD

A. DELTA III Camera Configuration - As a result of an accelerated test program, this configuration demonstrated a system NRO 25X1 compatibility with the U-2R and was declared Operationally Ready (OR).

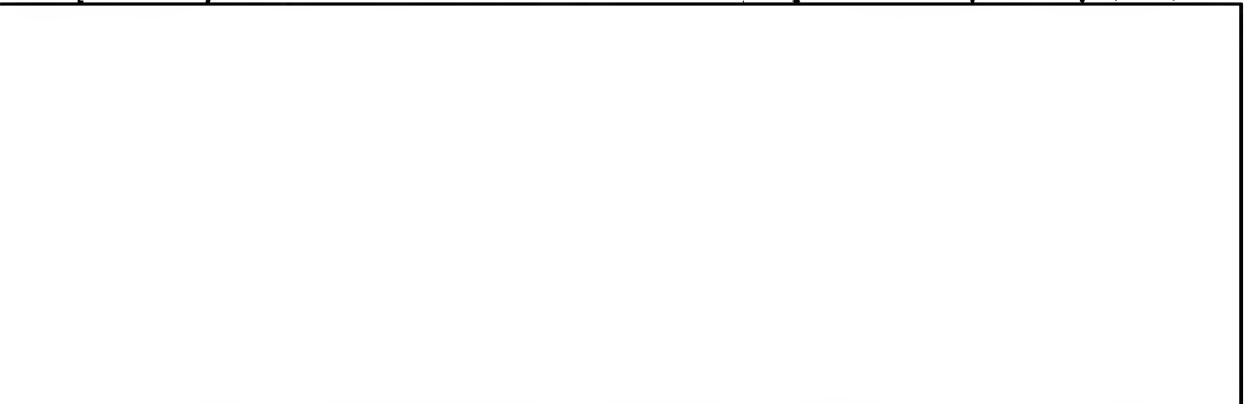

C. Thermal Stabilization - In order to insure proper thermal stabilization in the U-2R "Q-Bay" prior to the earliest required camera "ON" time during flight operations, a decision was made to order insulation in the "Q-Bay" hatches and procure preconditioning ground equipment.

25X1A

OXCART/IDEALIST

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

6409-69

TAB B, Section 1

Page 4

25X1A

D. Haze Attenuation Study - Further contractual work is being held in abeyance until such time as additional information is received from Eastman Kodak as a result of Red Dot Tests.

Initial polarizer filter tests indicate very little additional information is gained when filters are used to reduce effects of haze, this is particularly true when filters are utilized with panoramic type cameras.

IV. LIFE SUPPORT

A. Pinger Assembly - The Pinger currently installed in the U-2C/R aircraft will be replaced with a longer range Pinger in the nose and tail of the aircraft. In addition, the longer range Pinger will be installed on either the pilot seat pack or the pilot's ejection seat.

B. Silver Zinc Battery Life - Results of a test project conducted at Detachment G on the silver zinc battery indicate that these batteries can remain installed until the battery test reveals the open circuit voltage is below 29.1V or when the emergency battery "ON" warning light has illuminated during flight.

C. Liquid Oxygen (LOX) Converter System - The U-2R LOX Converter System is in the final stages of testing and evaluation. It appears at this writing that the system now undergoing tests will provide a longer range and trouble free system.

V. U-2R HIGHLIGHTS

A. Aircraft 051 - Lockheed Aircraft Corporation completed the performance of oxygen re-light tests using this aircraft. It is planned to employ the aircraft (two flights) for completion of the auto-pilot tests. Following these, the aircraft will be placed in maintenance and receive [redacted] and Integrated Display Panel modifications. It will be operationally configured and ready by late May 1969.

25X1D

OXCART/IDEALIST

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION

25X1A

25X1D

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

OX CART/IDEALIST

6409-69

25X1A

TAB B, Section 1

Page 6

25X1D



VII. GENERAL RESEARCH AND DEVELOPMENT

A. GENERAL R&D

1. Drag Reduction Program - Results of the wind tunnel test program conducted at the NASA Ames Research Center during the second quarter of FY-69 were analysed and verified the results previously acquired in the Monterey wind tunnel (15% - 20% induced drag reduction). However, discussions with Lockheed Aircraft Corporation (LAC), revealed that the optimum Monterey/Ames Configuration was not structurally compatible with the U-2R. A structurally acceptable redesign was

25X1A

OX CART/IDEALIST

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
CLASSIFICATION

TOP SECRET

Approved For Release 2002/08/26 : CIA-RDP68B00724R000100150037-5

6409-69

TAB B, Section 1

Page 7

25X1A

subsequently tested [] wind tunnel but the configuration could only provide a 4% - 8% induced drag reduction. Since the practical constraints imposed on this diffuser configuration cause a significant reduction in effectiveness, consideration must be given as to the advisability of continuing this program.

25X1A

2. High Altitude Relight Program - The flight test of the high altitude relight system was conducted during the period 20 February 1969 to 24 March 1969 and included a total of 7 test flights in the U-2R aircraft. Three types of hardware changes over the basic J75-P-13B engine configuration were included in the modified test engine. These included sealed burner can crossover tubes, two additional igniters in the combustion chamber and oxygen injection to all four igniters. Tests were conducted utilizing all three engine hardware modifications and various combinations of these modifications, with the following results: Use of the two additional igniters appears to have no effect on relight altitude. Data indicates that the sealed crossover tube modification without oxygen injection would provide a repeatable capability to relight with good acceleration at an altitude of 50,000 feet and a flight Mach number of .75, and that the oxygen injection buys an additional but less repeatable 6000 to 8000 feet. The maximum altitude at which successful relights have been obtained without any of the above relight hardware is 43,000 feet. These were under controlled conditions. Consequently, the U-2R flight manual has indicated that air-starts are possible at altitudes of 43,000 feet, but that above 40,000 feet acceleration will be slow. The sealed crossover tubes therefore have increased the repeatable engine relight altitude in the U-2R from 40,000 feet to 50,000 feet.

3. Methane Fuel Technology - The program on methane fuel technology for advanced air breathing engines has been resubmitted to the DNRO for approval. Propulsion Systems Division, OSA reviewed the proposed program during a second meeting on this subject with Mr. Joe Jones, Assistant Secretary of the Air Force for R&D on 29 January 1969. Mr. Jones voiced his support and approval of the program and recommended the resubmission to DNRO. The program involves a demonstration effort operating a gas turbine engine on two phase methane fuel utilizing "breadboard" fuel system components.

OXCAR/IDEALIST

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION

Approved For Release 2002/08/26 : CIA-RDP68B00724R000100150037-5

TOP SECRET

25X1A

TOP SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

6409-69

25X1A

TAB B, Section 1

Page 8

25X1D

D. MISCELLANEOUS

Snow Survey Study - At the request of the Environmental Science Services Administration, Department of Commerce, through COMEREX, OSA has been obtaining coverage of the snow cover in the Sierra Nevada range of eastern California. This program, being

25X1A


OX CART/IDEALIST

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION

TOP SECRET

Approved For Release 2002/08/26 : CIA-RDP68B00724R000100150037-5



6409-69


25X1A

TAB B, Section 1

Page 9

conducted through the third and fourth quarters of FY-69, is a part of an ESSA evaluation of the capability of photography from an earth Resources Satellite to obtain information for the forecasting of water supply available from snow cover. Small scale (1:280,000) photography is being obtained at monthly intervals in two instrumented regions in the Sierra Nevada mountains. Three successful flights have been made to date; approximately three more are programmed.

25X1A



OX CART/IDEALIST

TOP SECRET

Approved For Release 2002/08/26 : CIA-RDP68B00724R000100150037-5

GROUP 1: EXCLUDED FROM
AUTOMATIC DOWNGRADING
AND DECLASSIFICATION

25X1C

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

Next 2 Page(s) In Document Exempt

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

☐ UNCLASSIFIED☐ INTERNAL
USE ONLY☐ CONFIDENTIAL☐ SECRET

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5

ROUTING AND RECORD SHEET

SUBJECT: (Optional)

THIRD QUARTER FY-69 -- PROGRAM PROGRESS REPORT

6409-69

25X1A

FROM:

EXTENSION

NO.

8899-69

25X1A

DATE

10 April 1969

TO: (Officer designation, room number, and building)

DATE

OFFICER'S
INITIALS

COMMENTS (Number each comment to show from whom to whom. Draw a line across column after each comment.)

25X1A

1.

D/O

10 Apr

approval

2.

D/M

11 Apr

coordinate

3.

R&D

1 Apr

"

4.

EO

4/11/69

info

5.

DD/SA

11 Apr

approval

6.

D/SA

15 Apr

approval & signature

7.

SAS

reproduction & distribution

8.

9.

10.

11.

12.

13.

14.

15.

Approved For Release 2002/08/20 : CIA-RDP68B00724R000100150037-5
